



LAKE DUNLAP WATER CONTROL & IMPROVEMENT DISTRICT

LDWCID Member Update

September 30, 2021

Day 870

Fellow LDWCID Members;

Your LDWCID Board held a public hearing September 21, 2021 regarding the adoption of the final tax rates for the 2021 Tax Year. The new tax rates will be 10 cents for the maintenance tax and 10 cents for the contract tax, for a total tax of 20 cents per hundred dollar tax valuation. The maintenance tax is for the operation of the LDWCID while the contract tax covers the payment of debt service to GBRA for the borrowed funds to repair the dam. The tax rates have been forwarded to the County for inclusion in the upcoming tax renditions.

We also approved the District Information Form which is supplied to prospective property buyers within the District to inform them of the LDWCID Tax.

In addition, we adopted our formal 2021-2022 budget.

All of this information can be viewed on the LDWCID website.

Construction progress continues on the restoration of our dam!

Lake Dunlap Dam Restoration Project Update

Work on the Lake Dunlap Dam Reconstruction project continues to progress with critical path activities. LDWCID Technical Committee members continue to participate in Monthly Progress meetings along with GBRA, Black & Veatch Engineers, and Zachry Construction. In addition, the

Technical Committee members receive a Daily Report each morning from the Black & Veatch onsite inspector. As with all construction projects, much of the administrative work occurs behind the scenes, but the following is a recap of significant activities at the jobsite.

Recent Activities:

- 1) Continued work on procurement and submission of critical submittals for all aspects of the project including the Hydraulic Crest Gates.
- 2) Installation of the Temporary Crane Trestle. (Bridge) This activity is no longer on the schedule's critical path and is complete.
- 3) Installation of Bay 1 Driven Sheet Pile (Cofferdam) This is critical path work and is completed.
- 4) Continued work on the Emergency Spillway and earthen Dam Hardening. This is non-critical path work.

Upcoming Activities:


- 1) Grout Injection to seal off Cofferdam after Sheet Pile installation.
- 2) Dewatering and excavation of Bay 1 between the Cofferdam and existing Dam structure.
- 3) Demolition of existing Bear Trap gate in Bay 1.

Below are a few photos of the construction and old gates courtesy of Larry Johnson:

© 2021 Larry Johnson






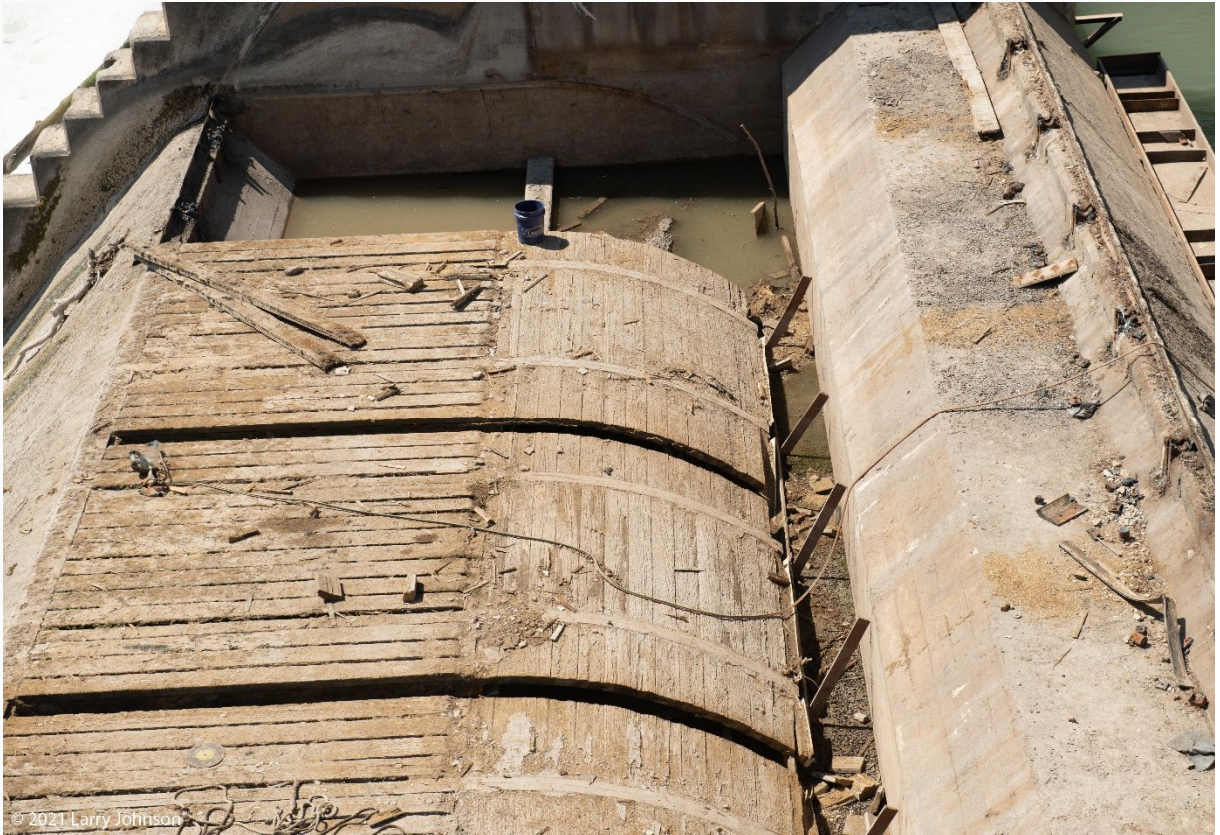

© 2021 Larry Johnson



© 2021 Larry Johnson

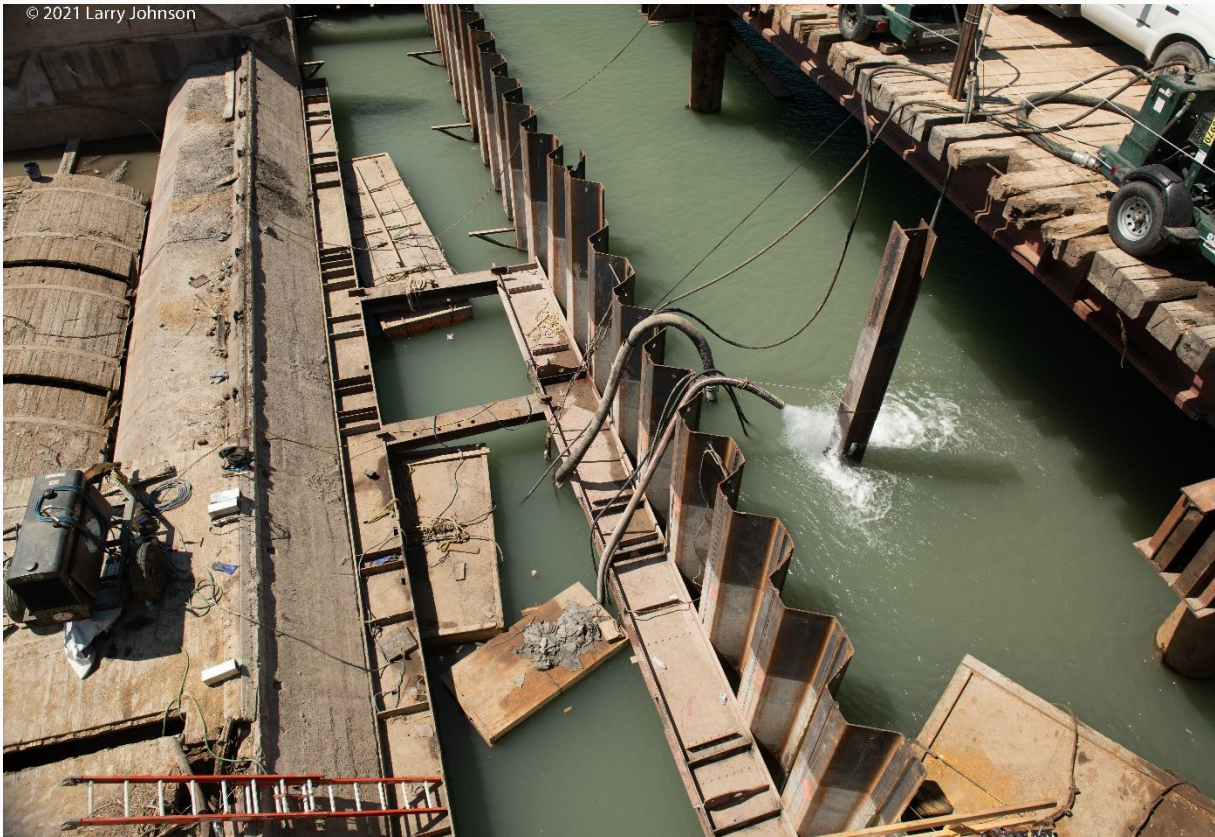

There are many points of unofficial news and unverified gossip out there. The only true source is www.LakeDunlapWCID.org.

Your LDWCID Board:

Doug Harrison, President

J. Harmon, Vice President

Gary Schaub, Treasurer

Harry Moeller, Technical Committee Leader & Asst. Secretary

Larry Johnson, Secretary
